



"2013, Year of Institutional Loyalty and Centennial of the Mexican Army"

227-21000-21600-- 2438 -2013  
Poza Rico de Hgo., August 21, 2013

PEMEX EXPLORACION Y PRODUCCION  
Gulf Tertiary Oil Production Asset  
APATG Contract Residence

CC. Raúl Lopez Gallegos  
Legal Representative

AT"N: Carlos Carranza Rodríguez  
Contract Construction Superintendent 424043804  
BISSELL Construcciones e Ingeniería S.A de C.V.  
MWS Management, Inc. (Joint Proposal)


Subject: Response to the official letter 44-2013 and status report of the BISSELL 1 equipment for contract 424043804

Regarding Contract No. 424043804, related to: "Comprehensive Works for Interventions to Ground Wells in the Northern Region (package I), executed with BISSELL CONSTRUCCIONES E INGENIERÍA S.A de C.V. AND MWS MANAGEMENT, INC. (Joint Proposal) and in response to official letter BISSELL-MWS-44-2013 dated August 20, 2013; we inform you of the status of the equipment called BISSELL 1 according to the review performed last Monday, August 19, 2013.

Figure 1



227-21000-21600-- 2438 -2013  
Poza Rico de Hgo., August 21, 2013

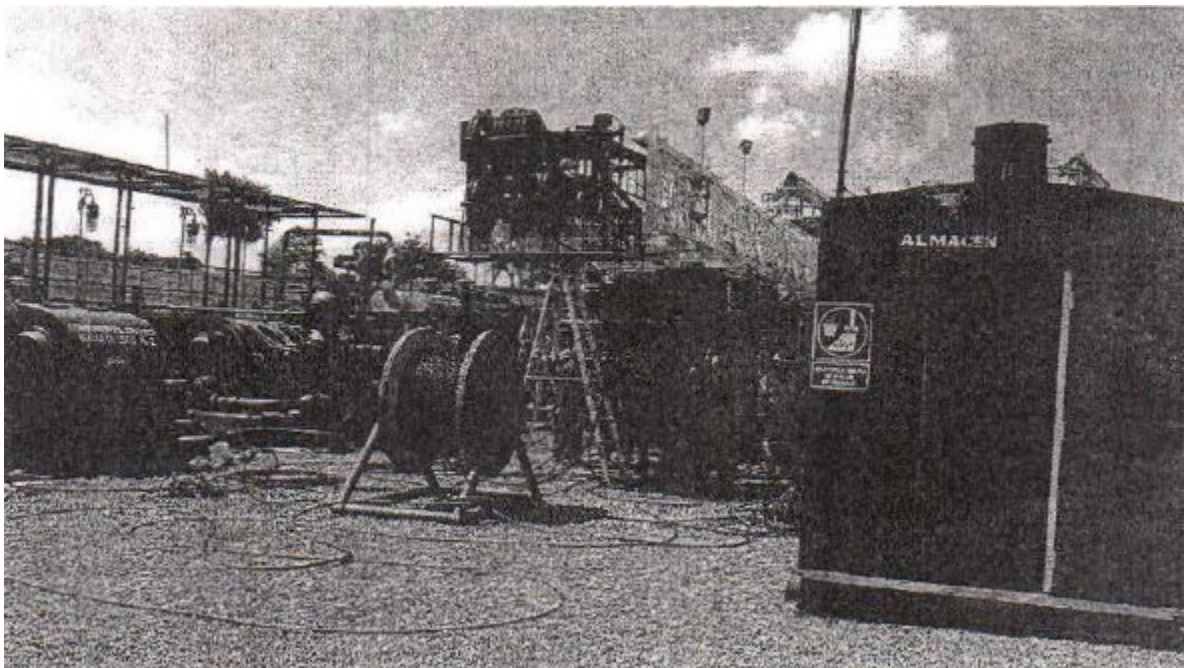

The equipment is not yet complete in all its equipment components

Figure 2




The pumps have not been subjected to any operation check and there are no certifications for them.





227-21000-21600-- 2438 -2013  
Poza Rico de Hgo., August 21, 2013

Figure 3

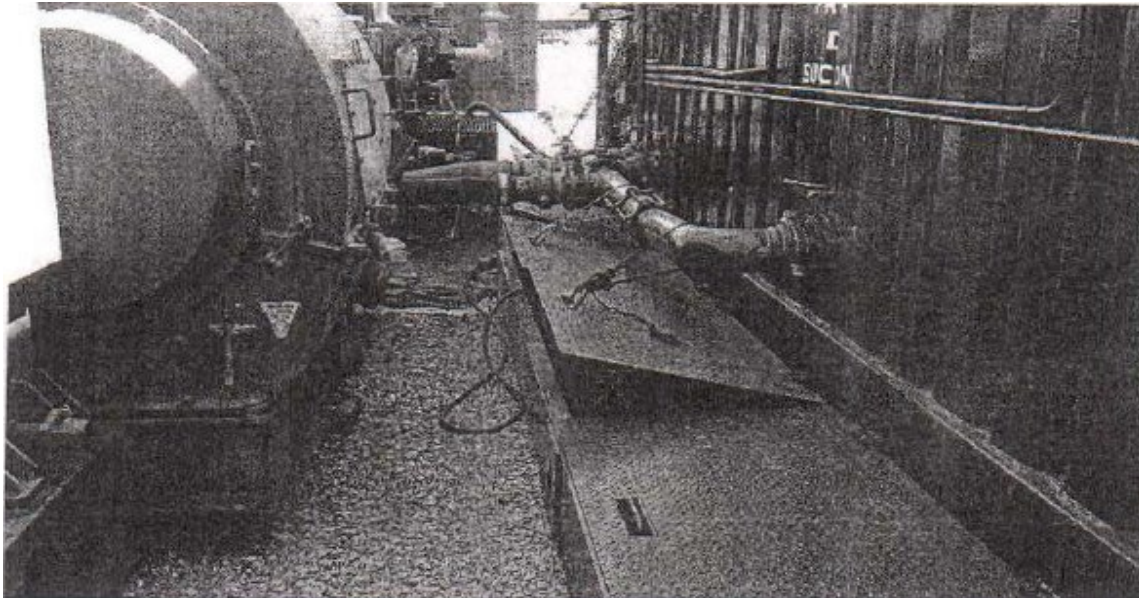

The installation of connections is still in process.  
Lacking the technical reports of the same.  
and the corresponding certifications.


Figure 4



**227-21000-21600-- 2438 -2013**  
**Poza Rico de Hgo., August 21, 2013**

The cut-off dam is damaged and completely corroded.

Figure 5

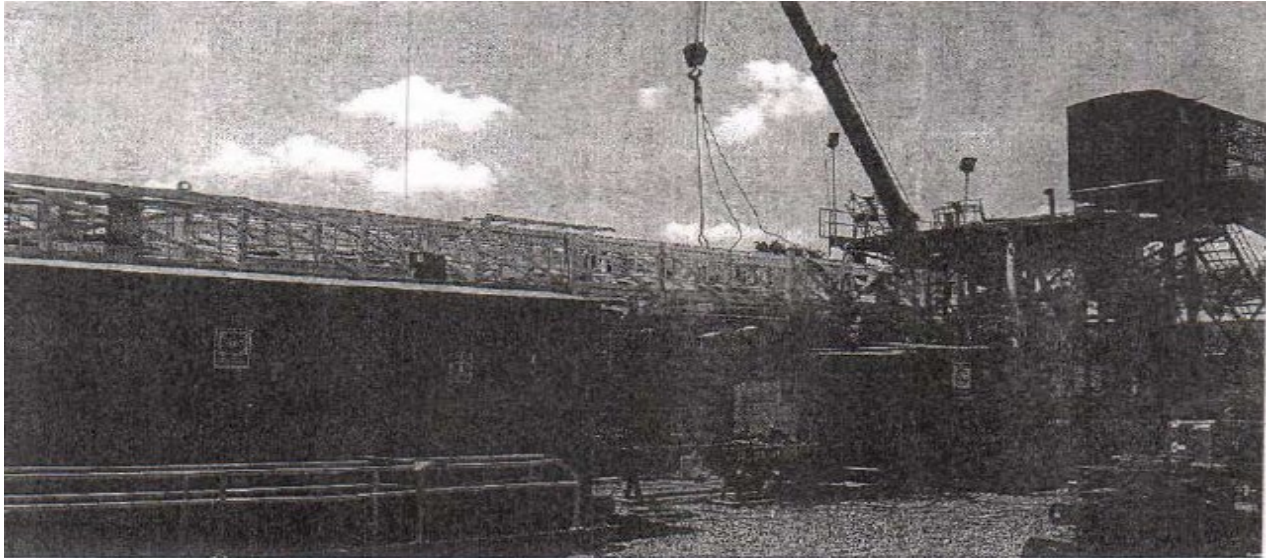

It is noted that several components of the equipment are still in the process of repair.  
of repair of various components of the equipment.

In addition to the above, it should be noted that to date the technical books of the equipment are not available, the certifications of the components have not been received, and the technical details of the modifications made to the equipment have not been delivered to this Contracts Residence.

I do not omit to mention that the equipment has not yet been discharged by the Well Design and Engineering area and that to date no Check List has been made to the equipment, which are also considered reasons for not starting the drilling works.

Therefore, it is important to point out that PEP is not responsible for the decisions made by the contractor.

Without further ado, I would like to take this opportunity to send you my best regards.

Sincerely,



Oscar Hernández Bartoluchi  
APATG Contract Residence



**227-21000-21600-- 2438 -2013**  
**Poza Rico de Hgo., August 21, 2013**

ESCH  
AAV

C.c.p. Leandro Sanchez Mendiola - Gerencia de Servicios a Proyectos RN  
Juan Manuel Riaño Caraza - Administrador APATG  
Julio César López Martínez - E.D. Grupo Multidisciplinario de Servicios por Contratos a Pozos  
José Luis Trujano Vargas - E.D. Jefatura Diseño e Ingeniería de Pozos DIP APATG  
Gabriel Armando Martínez Torres - E.D. Diseño de Perforación DIP APATG  
Expediente Consecutivo

