Date: August 14, 2013



"2013, Year of Institutional Loyalty and Centennial of the Mexican Army."

Submitter Activo Producción Aceite Terciario

del Golfo Residence of Contracts

APATG.

Oscar Hernández Bartoluchi

E.D. Residencia.

Present

Reicpient Project Services Management, R.N.

Leandro Sánchez Mendiola

E.O. Management.

Present.

Subject Drilling Equipment, Contractor Bissell

Constructions.


In relation to contract No. 424043804 of Direct Award, formalized between the contractor BISSELL Construcciones e Ingeniería, S.A de C.V. and Pemex Exploración y Producción, for the execution of the "Integral Works for Onshore Well Interventions in the Northern Region (Package 1) of Direct Award"; I hereby inform you the following:

In order to certify and validate the progress in the execution of the works related to the Drilling and Completion of the wells detailed below:


- Bissell Equipment 1, Located at Remolino 3998 of Remolino Macroperator 3952 and based on Work Order No. 003/B3804/2013 formally delivered by means of official letter 227-21000-21600-2010- 2013 dated July 12, 2013 to start on July 19, 2013 and completion date August 19, 2013.
- Bissell Equipment 2, Located at Remolino 2906 of Remolino 2968 Macroperator and based on Work Order No. 004/B3804/2013 formally delivered by means of official letter 227-21000-21600-2048- 2013 dated July 18, 2013 to give start on July 25, 2013 and completion date August 25, 2013.

Therefore, on August 14, 2013, a visit was made to the rehabilitation workshops of the aforementioned contractor, located on Highway 180 Poza Rica - Tuxpan (Poza Rica - Tihuatlan section, Rancho Santa Elena lot 32 and 33 "Zapotalillo", where missing equipment was observed, dismantled, as shown in the following photographs:








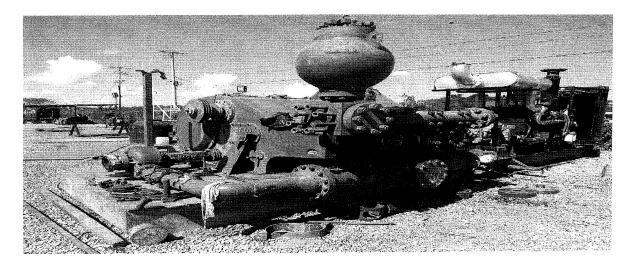


• Sludge pump. -Lack of coupling with the motor as well as tightening of connections and belts.

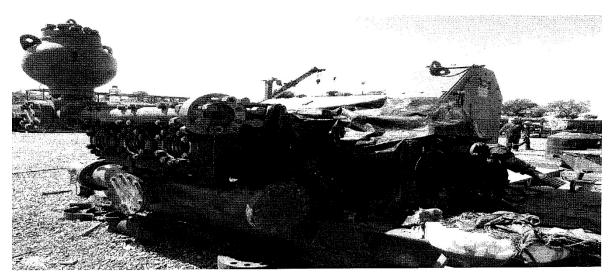


• Sludge pump. -Lack of coupling with the motor as well as tightening of connections and belts.








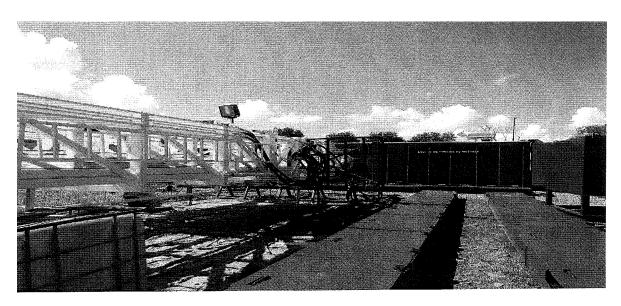


• Equipment Mast: - To be wired, connected and tested.

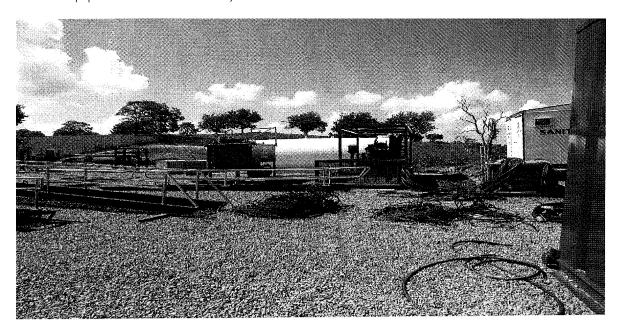


• Bomba Koomey, conexiones faltantes, calibración, instrumentación y pruebas.








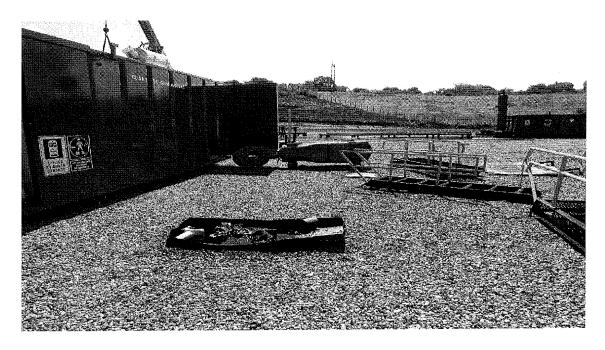


• Traveling Pulley: -Lack of installation, wiring.

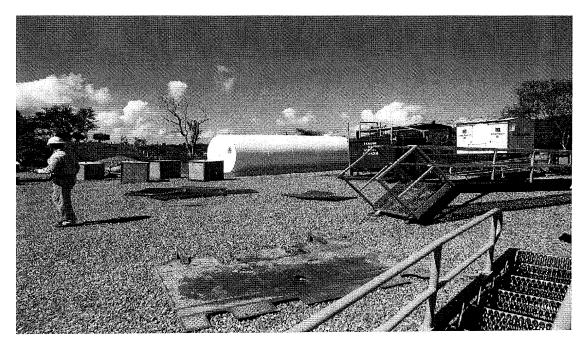


• Vacuum tank missing tests.







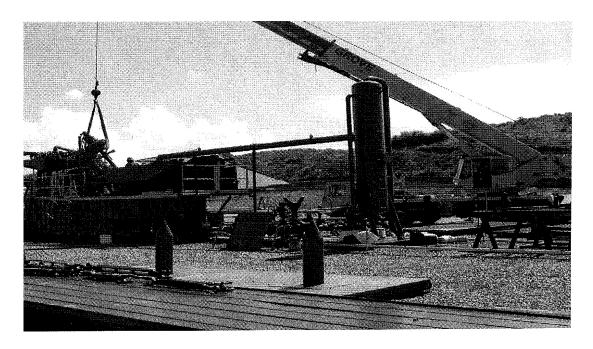

• Sludge dams, agitation dams and gas-sludge separators: - Lack of connections, gaskets.




• Pumps and sludge dams: - lack of installation of bottom guns General tests.




+ 6



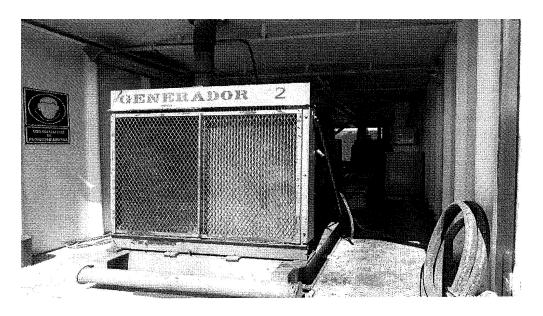


• Generator: - Lack of general connections, lack of another air compressor.

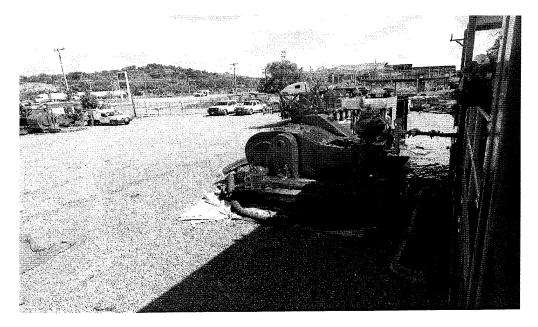

• Sludge Pump: - Missing connections, packaging and tests.







Atentamente,

Oscar Hernández Bartoluchi E.D. Residente.

C.c. Pedro Rojas Gómez.- E.D.- Grupo Multidisciplinario de Servicios por Contratos a Pozos, R, N. Expediente consecutivo

Elaboro: Antonio Vicente Ayud.
